

Lee's Summit High School Renovations & Addition Monthly Construction Report



This Month

July

Renovation Areas:

- Completed overhead mechanical, electrical, and sprinkler systems in North B Building
- Installed new drywall walls and soffits
- Install paint, ceiling grid, and epoxy flooring

Addition:

- Punch list items in Addition 1
- Installed underground utilities for Addition 2
- Continued with footings and building pad



Area J Windows

Next Month

August

Renovation Areas:

- Complete remaining finishes—flooring, final paint, cleaning
- Complete punch list items

Addition:


- Complete asphalt bus loop
- Set steel for Addition 2
- Pour concrete floor slabs for Addition 2



Chiller Yard Wall



Area H Hallway—MEP Install/Brick Wall Infill

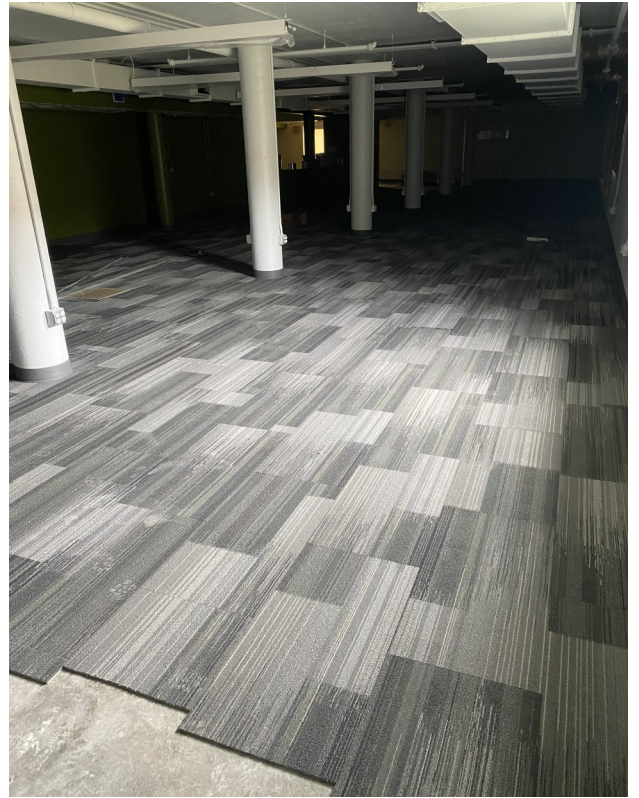

B Building Basement—Carpet Install



Area A/B Building Drawing Classroom



Area G Level 2—UG Plumbing install and concrete placement
